

You may send as a PDF once completed

Access Improvement Grant – Reporting template

Please use a new sheet for each project / location.

Please copy and paste entire page for more templates.

Project title:	Location:
Glyndwr's Way National Trail	Llanwddyn

Description of works completed:
No planned activity in year 2

Access Improvement Grant – Reporting template

Please use a new sheet for each project / location.

Please copy and paste entire page for more templates.

Project title:	Location:
Wye Valley Walk Improvements	Mid & South Powys

Description of works completed:
• Survey entire section of WVV in Powys (62km), in order to build action plan for targeted improvements to meet Wye Valley AONB plan of relaunching WVV for 50th anniversary in 2023, will feed into new WVV guide and website. • Targeted improvements to WVV based on survey, to include; • Replacing stiles with gates, subject to landholder agreement • Replacing signage, surface improvements • Restoration Of Washed Out 590m Section of Wye Valley Walk Nov update: - The CAMS web system is now operational and mobile devices have been purchased (using separate funding) - Surveying and CAMS Web training of volunteers has begun and will continue in a rolling programme. - Surveys underway by the trained volunteers – to identify structures for improvement, subject to landowner consent. - Officers have also carried out some survey work, having previously purchased gates and posts ready for installation (2023/24) - Significant byway surface works completed early summer '23 March update - Surveying by volunteers is now complete. - Four further CAMS Web training sessions for volunteers have taken place (Feb '24). - Implementation of requirements identified in the surveying of the route – some gates, signage etc. Material purchased for some of the on-site installations by existing

volunteers May-July 2024.

- Materials for steel bridge purchased and contractor appointed to install bridge as soon as weather permits (March/April '24) - ground needs to dry up so we can get across fields without damage. Bridge work to include a new galvanised steel structure with accompanying bank reinstatement/protection work, on existing concrete abutments. Bridge location - WVV on FP 040/4/1 east of PENTREBACH FARM, LLANFIHANGEL BRYN PABUAN, BUILTH WELLS, LD2 3SF.
- Purchase of materials (recycled plastic products) for boardwalk improvement on WVV.
- Materials to support the recycling of some old bridge materials 500m upstream.

Spend breakdown:

Total	Year 2 / claims		Notes
	Nov	March	
Budget	£75,946.57		
Activity 01/04/23 -30/09/23	£50,051.17		
Activity 01/10/23 - March 2024		£39,330.84	
Staff 01/04/23 - March 2024		£5,727.76	
Total spend @ March 2024	£95,109.77		

Variance: +25%

Explanation:

- Additional costs have been incurred following the discovery of a problem with a bridge that we hadn't anticipated, and it's fundamental to the accessibility of the Wye Valley Walk.

Outputs:

(i.e. section 7 of the workplan.)


- Full survey of the entire WVV within Powys
- Improvements to signage along the entire route (62km), including refreshing all waymarking
- Improvements to path surface – 590 metres.
- 590m of Restricted byway will be restored to an access for all condition. Previous improvement works have, given the topography and hydrology at this site, not been durable. The works in this project are intended to be sufficiently robust and long lasting and allow for all lawful user over the Restricted Byway.
- Improvements to 10 access structures to make the route more accessible to all, subject to landowner agreement

Photographic evidence – before / during:



Photographic evidence – after (not needed if an uncompleted multiyear project):



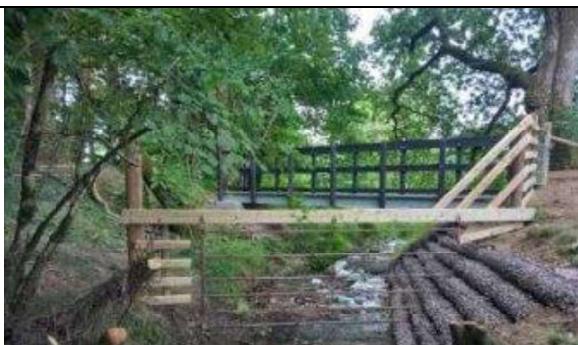

Access Improvement Grant – Reporting template

Please use a new sheet for each project / location.

Please copy and paste entire page for more templates.

Project title:	Location:
Presteigne Phase 2	Presteigne - SO 3147 6401 & SO 3077 6337

Description of works completed:

- Significant improvements have previously been made to the replacing and upgrading the riverside path in Presteigne; further additional works are needed to address the river crossings along this route, which are not passible in winter flows.
- Works to investigate and implement physical improvements in a dynamic river channel, forming river crossings along the route. Works will require Land Drainage Consent and a robust design as the river channel is very reactive and can frequently be fully submerged.

Nov update

- Bridge and materials purchased October 2023
- Contractor engaged for bridge installation and removal of steps, create bank and slope – physical works to take place when weather permits (the area suffers from flooding)
- Additional materials for site work earmarked.

March update

- The path used to follow the river and cross three times via stepping stones/ fords. Work has realigned the path along a single bank and replaced the three river crossings with one bridge above high water.
- The new metal and recycled plastic bridge has been installed by the contractor at a level so that it does not impede the river's flow; on the northern river bank the ground has been landscaped to the bridge and recycled plastic retaining boards used to hold it in situ.
- On the southern bank it was initially planned to install a ramp willed with gravel from site; however with concerns that this would not form a long lasting solution, as it would be vulnerable to the high river levels (which are higher than we have initially believed while specifying the original job), we decided that steps would be a better option.
- The proposed steps will be formed of a metal frame and recycled plastic planks to stand on, giving a long life option, and still allowing high water levels to pass through the steps. The contractor is proposing to cap the bridge abutments to prevent loss of gravel should the river overtop them, again future proofing the works further.
- All work is complete other than the ramp (now steps), leading from one side of the

bridge. Design of the steps in is progress and will be part funded outside of the AIG programme.

- Community feedback has been very positive with acknowledgement given to the transformation to an accessible and well used community route.

Spend breakdown:

Total	Year 2 / claim		Notes
	Nov	March	
Budget	£16,500		
Activity 01/04/23 – 30/09/23	0.00		
Activity 01/10/23 – March 24		£24,233.52	
Staff 01/04/23 - March 2024		£749.94	
Total spend @ March 2024	£24,983.46		

Variance: +50.6%

Explanation:

- Work to the path and bridge has been extensive.
- Given the conditions in/around a river of increasingly fluctuating water levels and general damp surrounds, materials chosen for the bridge construction (recycled plastic) have resulted in higher costs but provide a much better long-term option.

Outputs:

(i.e. section 7 of the workplan.)

- Improvements to river crossings
- Improvements to 270 metres of path surface

Photographic evidence – before / during:

Ford – closest to the road – removed by path realignment





Steps have been removed and replaced with a realigned path on the left of this photo at the top of the bank



I couldn't actually get to where the photo above were taken this day, even in wellies, the water was too deep and swift



looking upstream from the bottom of the steps

Photographic evidence – after (not needed if an uncompleted multiyear project):

Start of new path



Metal pole is fingerpost in both photos



Replacement of post and rail across the top of the bank also underway

2nd ford removed by re-aligned path and bank works



Works on left of photo (looking downstream)



Before works and in spate (photo looking downstream)



Contractor works 1




works 2



already drying out

3rd ford replaced with bridge – note the large willow tree in the background

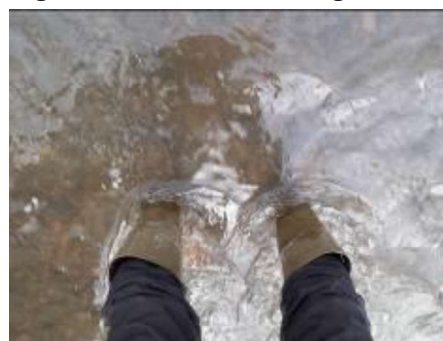

too deep to cross even in wellies this day



bridge looking downstream



bridge looking upstream



start of path by Joe Deakins Road



Access Improvement Grant – Reporting template

Please use a new sheet for each project / location.

Please copy and paste entire page for more templates.

Project title:	Location:
Newchurch Area Improvements	Newchurch area SO 2405 5033

Description of works completed:
No planned activity in year 2

Access Improvement Grant – Reporting template

Please use a new sheet for each project / location.

Please copy and paste entire page for more templates.

Project title:	Location:
South Rads Equestrian Improvements	Glasbury, Clyro, Painscastle community areas

Description of works completed:

No planned activity in year 2

March update:

- A little staff time utilised for assigning paths to the volunteers for surveying and analysing the results, ahead of year 3 work programme.

Spend breakdown:

Total	Year 2 / claim		Notes
	Nov	March	
Budget	£0.00		
Activity 01/04/23 – 30/09/23	£0.00		
Activity 01/10/23 – March 24		0.00	
Staff 01/04/23 - March 2024		£141.72	
Total spend @ March 2024	£141.72		

Outputs:

(i.e. section 7 of the workplan.)

Photographic evidence – before / during:

n/a

Photographic evidence – after (not needed if an uncompleted multiyear project):

n/a

Access Improvement Grant – Reporting template

Please use a new sheet for each project / location.

Please copy and paste entire page for more templates.

Project title:	Location:
Promenade / Fenni Field Path Improvement, Brecon	Brecon

Description of works completed:

No planned activity in year 2

Access Improvement Grant – Reporting template

Please use a new sheet for each project / location.

Please copy and paste entire page for more templates.

Project title:	Location:
Disabled Access Ramp into the Recreation Ground, Llangattock	Llangattock

Description of works completed:

No planned activity in year 2

Access Improvement Grant – Reporting template

Please use a new sheet for each project / location.

Please copy and paste entire page for more templates.

Project title:	Location:
Offa's Dyke Park improvements	Knighton

Description of works completed:

- The work involves path improvements in the park, with gabions and path surface improvements. This is a very popular park close to the town centre and linking to the Offa's Dyke Path National Trail; a set of steps linking with the Trail will be improved. The aim is to increase the accessibility of the greenspace for residents and visitors. (Moved from year 3 to year 1)

Nov update:

- Materials purchased in year 1 (22/23)
- Contractor implemented work in early summer 2023.
- Project completed May 2023

Spend breakdown:

The Year 1 project budget had been increased using underspend from the access to water project.

Total	Year 2	Notes
Budget	nil	
Activity 01/04/23 – 30/09/23	nil	
Staff 01/04/23 - March 2024	nil	
Total spend @ March 2024	nil	

Outputs:

(i.e. section 7 of the workplan.)





The project is completed earlier than anticipated, as this was scheduled to be a year 3 project.

- Improvements to handrails and footpath edgings.
- Improvements to 800 metres of path surface.
- Install 34 metres of gabion baskets.

Photographic evidence – before / during:

Photographic evidence will follow

Photographic evidence – after (not needed if an uncompleted multiyear project):

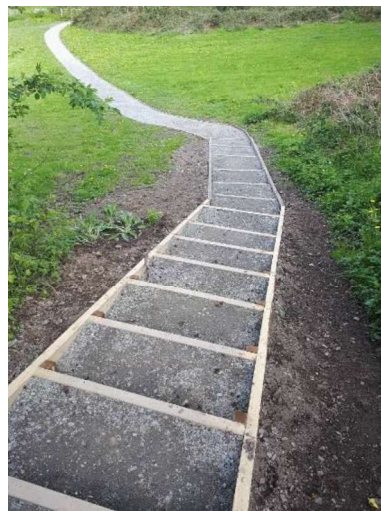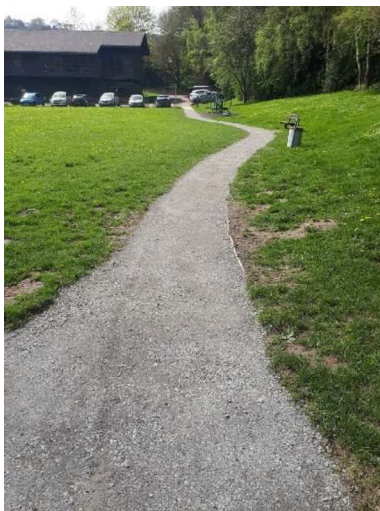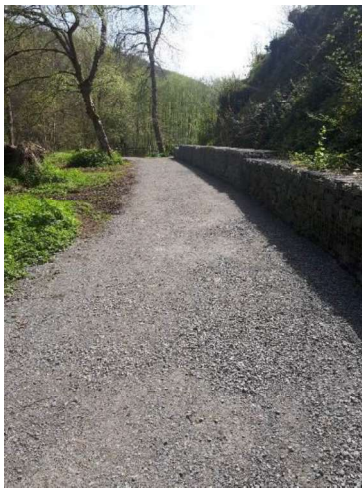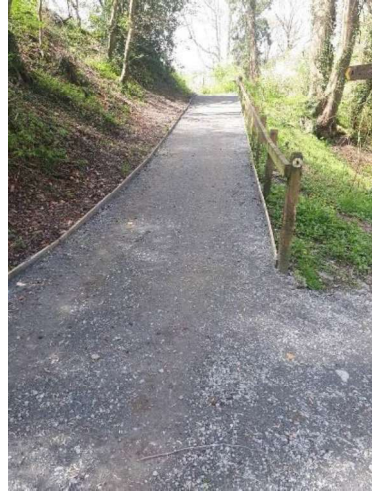

Access Improvement Grant – Reporting template

Please use a new sheet for each project / location.

Please copy and paste entire page for more templates.

Project title:	Location:
Volunteer Handbook for Publishing on Internet	Powys

Description of works completed:

- To produce a handbook to facilitate and support community-based volunteer groups to manage their PROW and Greenspaces more effectively, to include; MoA, Guidance on Legislation, Standard Letters, Info on procedure, Furniture installation info. The handbook will be produced by an external consultant and managed by PCC staff.

Nov update:

- Structural drawings (installation standard for different pieces of path furniture e.g. pedestrian gate) prepared in year 1 are being translated and Welsh versions created.
- Stakeholder engagement around requirements/content are being planned - countryside volunteer working group, Local Access Forum and others.

March update:

- Stakeholder engagement is nearing completion (Jan-March 24), with feedback around requirements for the document sought from the Local Access Forum, Volunteer working Group, all 220 existing volunteers, members of the Countryside Access team and other key individuals.
- Feedback is collated and planning / delivery of the content will follow in 23/25.

Spend breakdown:

Staff time is being utilised in year 2 to prepare requirements /content for the handbook and engage with stakeholders.

Total	Year 2		Notes
	Nov	March	
Budget	£0.00		
Activity 01/04/23 - 30/09/23	nil		
Activity 01/10/23 – March 24		£0.00	
Staff 01/04/23 - March 2024		£155.42	
Total spend @ March 2024	£155.42		

Outputs:

(i.e. section 7 of the workplan.)

Outputs are being achieved in that drawings are being prepared of furniture installation as an easy to use reference document to include in the handbook.

The countryside stakeholder working group (now renamed the countryside volunteer working group) is meeting regularly and has been shown the first draft designs. Their input will be sought in spring 2024 around the content of the handbook.

Total	Year 2		Notes
	Nov	March	
Budget	£44,387.00		
Activity 01/04/23 - 30/09/23	£41,278.36		
Activity 01/10/23 – March 24		£868.25	
Staff 01/04/23 - March 2024		£813.00	
Total spend @ March 2024	£42,959.61		

Variance: -3.2%


Outputs:
(i.e. section 7 of the workplan.)

The outputs will be:

- Installation of a new bridge.
- Improvements to 130 metres of path surface, by resurfacing a section and removing steps where possible.
- Improved public access through replacing 5 stiles with gates.

Photographic evidence – before / during:



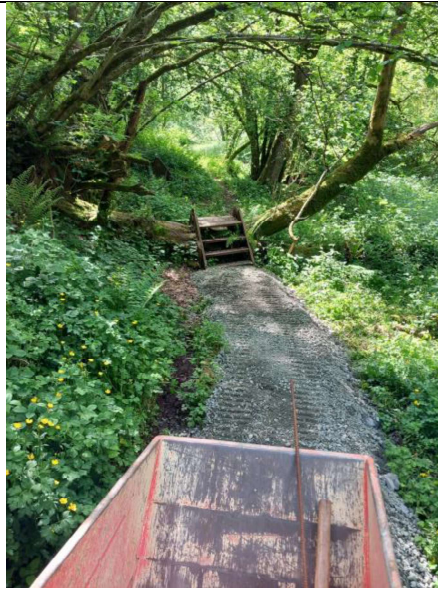

Photographic evidence – after (not needed if an uncompleted multiyear project):



Access Improvement Grant – Reporting template

Please use a new sheet for each project / location.

Please copy and paste entire page for more templates.

Project title:	Location:
Severn Way Improvements	North & Mid Powys

Description of works completed:

No planned activity in year 2

Access Improvement Grant – Reporting template

Please use a new sheet for each project / location.

Please copy and paste entire page for more templates.

Project title:	Location:
Trewern community access improvements	Trewern

Description of works completed:

- Making improvements to the footpath network around Middletown, Moel Y Garth and Criggion Hills.
- The aim is to negotiate improvements to the car parks at the Moel y Golfa Site and at Middletown Hill.
- It is also intended that a footpath creation be negotiated between the Middletown and Moel y Golfa Hills. This project work and ongoing maintenance of the improved paths will be supported by a community volunteer team.

Nov update:

- There has been discussion with the community around its aspirations
- Discussions are under way with the local community around the volunteering aspect.
- Early formal landowner negotiations are underway

March update:

- Clearance work carried out (non AIG), on a number of paths on Middletown Hill
- Survey work carried out on Moel y Golfa.
- Materials ordered for work with volunteers when the weather improves – improvements to signage and stiles to gates

Spend breakdown:

Total	Year 2		Notes
	Nov	March	
Budget	£22,541.52		
Activity 01/04/23 – 30/09/23	£0.00		
Activity 01/10/23 – March 2024		£5,346.19	
Staff 01/04/23 - March 2024		£16.01	
Total spend @ March 2024	£5,362.20		

Variance: -76.3%

Explanation:

- Anticipated works were greater than finally required by the community e.g the car park is an extensive project that requires planning approval, following agreement with NRW. Conversations are taking place around NRW making these improvements, if financially viable.
- Walking leaflet/information (digital) will now be picked up within complementary project activity.

Outputs:

(i.e. section 7 of the workplan.)

The outputs will be:

- General improvement of public rights of way network including stiles for gates/kissing gates and signage.
- Improved car park facilities.
- Creation of new footpath directly linking two 'honey pot' destinations.
- Creation of volunteer team to look after local public rights of way network.


Photographic evidence – before / during:

Photographic evidence will follow


Photographic evidence – after (not needed if an uncompleted multiyear project):



Flight 1

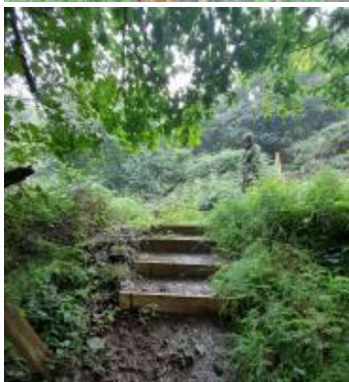

Flight 2

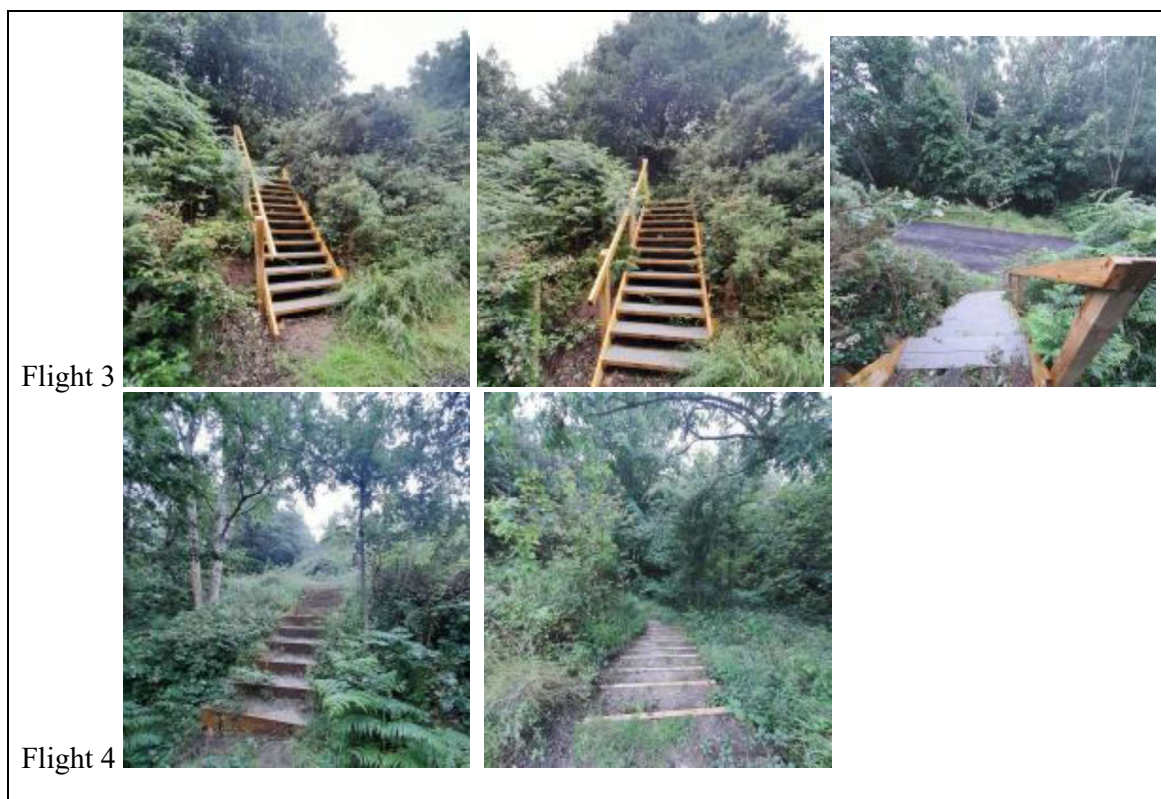

Access Improvement Grant – Reporting template

Please use a new sheet for each project / location.

Please copy and paste entire page for more templates.

Project title:	Location:
Dolfor Lock Bridge	Dolfor Lock Bridge, Montgomeryshire Canal, Newtown, Powys.

Description of works completed:
- To renovate a Montgomery Canal Bridge, Dolfor Lock. - Phase 1 – to involve engineering design investigations prior to preparing a full report and costings for the bridge renovation. Nov update: - Engineering design report is being compiled ahead of 31 Dec 2023 - Ecological survey requirements being investigated in line with the above. March update: - Engineering Design report being prepared in readiness for next years work programme. - Ecological – updated PEA during mid-winter. Further in-depth surveys (bat, great crested newts) will take place April-June. - Site meeting needed with engineer and other interested parties in April/May, following distribution of completed report.

Spend breakdown:

Total	Year 2		Notes
	Nov	March	
Budget	£8,401.00		
Activity 01/04/23 – 30/09/23	£0.00		
Activity 01/10/23 – March '24		£5,601.64	
Staff 01/04/23 - March 2024		£42.99	
Total spend @ March 2024	£5,644.63		

Variance – 32.8%

Explanation:

- Delivery of preparatory engineering reports and surveys slightly less than anticipated.

Outputs: <i>(i.e. section 7 of the workplan.)</i>
The project is at the stage of engineering investigation so outputs have not yet been achieved. These will be (in Year 3): • Bridge renovated and improved. • Legal diversion of footpaths brought into effect, with a new footpath being created over the bridge.

Photographic evidence – before / during:
Photographic evidence will follow on completion of works.
Photographic evidence – after (not needed if an uncompleted multiyear project):
Photographic evidence will follow on completion of works – Year 3

Access Improvement Grant – Reporting template

Please use a new sheet for each project / location.

Please copy and paste entire page for more templates.

Project title:	Location:
Rivers Wye and Usk information enhancement. Locations at canoe access and egress points to each river	River Wye, between Glasbury and Hay on Wye

Description of works completed:
There are two parts to this project, being: 1) <u>Production of information materials to support a Concordat Management arrangement for canoe launching at Upper Glas-y-Bont common, Glasbury:</u> • This element is linked to the outcomes of a Habitat Regulations Assessment which is being carried out and funded by the Council. • A draft report to inform the Habitat Regulations Assessment has been prepared and sent out for consultation to stakeholders. The responses are being reviewed and discussions are under way around a Concordat management framework. • The South Wales Outdoor Activity Group is preparing the content of the information

materials, on the basis of the content of the Code of Conduct that was in place previously and the draft report to inform the Habitat Regulations Assessment. Initial drafts of information have been prepared for discussion with other stakeholders.

2) Upgrade and replace existing signage at other access and egress points on the Rivers Wye and Usk:

- This piece of work is not progressing at the current time.

March update:

- A draft educational package has been prepared, with videos of the sensitive sites and rapids on the River Wye between Glasbury and Hay. The Habitat Regulations Assessment is nearing completion, with discussion around water levels ongoing. The broad framework for the Concordat has been prepared with further discussions around some detail. The remaining work will need to be completed in early 2024-25.

Spend breakdown:

Costs to cover South Wales Outdoor Activity Group staff time in initial review and exploration of the content of information materials to support a Concordat management arrangement (initially year 1)

Total	Year 2		Notes
	Nov	March	
Budget	£8,860.60		
Activity 01/04/23 – 30/09/23	£0.00		
Activity 01/10/23 – March 2024		£3,465.19	
Staff 01/04/23 - March 2024		£0.00	
Total spend @ March 2024	£3,465.19		

Variance: -60.9%

Explanation:

- Explanation: The budget is underspent in 2023-24 as there are Concordat details yet to be finalised. The remaining spend will fall in 2024-25 through revisions to the work plan, to be submitted by the end of April 2024.

Outputs:

(i.e. section 7 of the workplan.)

The outputs will be:

- 1 information sign installed at Upper Glas-y-Bont common to reflect sustainable canoe launch management arrangements
- Web based materials available for paddlesport operators, guides and group leaders with information around the access arrangements between Glasbury and Hay
- Web based materials available for hire clients, group members, independent paddlers, etc. with information around sustainable paddling between Glasbury and Hay
- 1 online training course developed for delivery to canoe operators using Glasbury to Hay section of the River Wye

Work is under way to develop the content of these materials based on the content of the draft Habitat Regulations Assessment and stakeholder discussions.

Upgraded signage installed at 8 launch points on rivers Wye and Usk – as noted above, this element is not progressing at the current time.

Photographic evidence – before / during:

None – Information materials under production.

Photographic evidence – after (not needed if an uncompleted multiyear project):

N/A

Access Improvement Grant – Reporting template

Please use a new sheet for each project / location.

Please copy and paste entire page for more templates.

Project title:	Location:
Builth Wells Circular	Builth Wells

Description of works completed:

No planned activity in year 2

Access Improvement Grant – Reporting template

Please use a new sheet for each project / location.

Please copy and paste entire page for more templates.

Project title:	Location:
Llechfaen Path Improvements	Llechfaen, Powys

Description of works completed:

The aim of the project is the improvement of the public path network radiating from Llechfaen Village.

- The project was intended to improve 6 local footpaths all radiating from the centre of the village to create individual circular walks and a pedestrian access to Groesfordd, where there is a local bus connection and a pub/restaurant.
- Later negotiations with some landowners encountered resistance in relation to some paths, in particular improving paths with gates or kissing gates as opposed to stiles. The project therefore had to be split into separate phases.

Activity to date:

Phase 1

- Footpath 3 – completed 22/23

Phase 2

- Completed early summer '23

Phase 3

- Completed early summer '23

Spend breakdown:

The total spend has been increased. In 2022-23, this made use of underspend from the Llangattock greenspace project. It is proposed that in 2023-24, increased budget costs will be met through an expected underspend in overall staff allocation cost.

Total	Year 2		Notes
	Nov	March	
Budget	£2683.85		
Activity 01/04/23 - 30/09/23	£6590.00		
Activity 01/10/23 – March 2024		£2765.08	
Staff 01/04/23 - March 2024		£859.98	
Total spend @ March 2024	£10,215.06		

Variance: +38%

Explanation:

- WG approval granted Nov '23
- Further costs have since been incurred (£2765.08) since the approval as further opportunities arose on site and final figures came through after the previous claim.

Outputs:

(i.e. section 7 of the workplan.)


- Improvements to appx 3km of PROW. Improved access for users with reduced mobility.

Photographic evidence – before / during:



Photographic evidence – after (not needed if an uncompleted multiyear project):

Llechfaen Phase 2 and 3

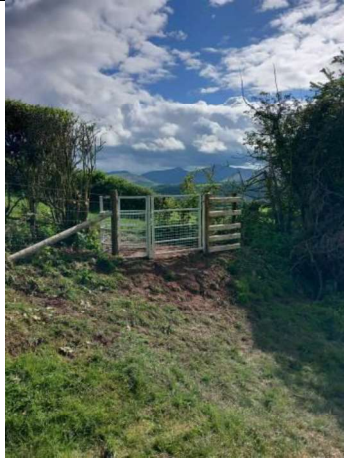

before and after



before and after

Access Improvement Grant – Reporting template

Please use a new sheet for each project / location.

Please copy and paste entire page for more templates.

Project title:	Location:
Aberllefenni bridge – upgrade from footbridge to bridle bridge	Aberllefenni

Description of works completed:

- Upgrading the current footbridge to a bridleway bridge. The river is the county boundary between Powys and Gwynedd; the public right of way leading to the bridge on the Powys side is a bridleway. The bridge is Powys County Council's responsibility.
- To date, a bridge specification has been drawn up, quotes received and the contractor selected. Negotiations with the landowner for access across their land to upgrade the bridge are drawing to a conclusion. An ecological survey and report are being prepared due to the proximity to an SSSI and ordinary watercourse consent is being sought for the removal of the existing footbridge. The spend in 2023-24 was less than expected as the abutments to the bridge did not require work.

Nov update:

- A bridge specification has been drawn up, quotes received and the contractor selected.
- Negotiations with the landowner for access across their land to upgrade the bridge are being finalised.
- An ecological survey and report are being prepared due to the proximity to an SSSI and ordinary watercourse consent is being sought for the removal of the existing footbridge.

March update

- Bridge kit has been purchased and contractor appointed for installation during May '24,

- to align with Ordinary Watercourse consent dates.
- Awaiting for consent to cross the land from NRW.

Spend breakdown:

Total	Year 2		Notes
	Nov	March	
Budget	£35,163.80		
Activity 01/04/23 - 30/09/23	£0.00		
Activity 01/10/23 – March 2024		£24,920.69	
Staff 01/04/23 - March 2024		£91.84	
Total spend @ March 2024	£25,012.53		

Variance: -29.8%

Explanation:

- The work has come in less expensive than first anticipated.
- Ecological surveys have been carried out with no fee.

Outputs:

(i.e. section 7 of the workplan.)

The outputs will be:

- Bridge installed, with upgraded access to include cyclists and horse riders
- Signage enhanced

The project is on track for completion by the end of March 2024.

Photographic evidence – before / during:

Photographic evidence will follow on completion of the project

Photographic evidence – after (not needed if an uncompleted multiyear project):

Photographic evidence will follow on completion of the project

Delay in work due to NRW consent delayed timeframe.

Access Improvement Grant – Reporting template

Please use a new sheet for each project / location.

Please copy and paste entire page for more templates.

Project title:	Location:
Llanbrynmair Community Project	Pennant, Llanbrynmair, Powys

Description of works completed:

- To enhance the connectivity of public rights of way in Llanbrynmair community, with installation of a new footbridge at Pennant and public path order and new infrastructure to improve connectivity of network around Llan and Llanbrynmair.

Nov update:

- The new bridge at Pennant has now been installed and the well-used path is open for use by the public (22/23), with positive resident feedback (particularly from a safety perspective, as it avoids use of the county roads to cross the valley, where there is no

- pavement)
- Negotiation is under way for the phase 2 work of path improvements.
- March update
- Due to lengthy and complex matters, the public path order remains ongoing.
 - Further community paths have been surveyed and landowner negotiations close to completion
 - Materials have been purchased ready for installation by volunteers when the weather permits - stiles to gates, removal of obstructions to path with provision of new gates (in several places), two sleeper bridges and one bridge.

Spend breakdown:


Total	Year 2		Notes
	Nov	March	
Budget	£13,000		
Activity 01/04/23 - 30/09/23	£0.00		
Activity 01/10/23 – March 2024		£12,170.82	
Staff 01/04/23 - March 2024		£2,186.94	
Total spend @ March 2024	£14,357.76		

Variance: +10.4%

Outputs: (i.e. section 7 of the workplan.)
The key outputs will be: • Improved access opportunities within the community and beyond transport to 15km of improved access routes as well as links to other multi user routes.

Photographic evidence – before / during:
Photographic evidence will follow on completion of the project
Photographic evidence – after (not needed if an uncompleted multiyear project):



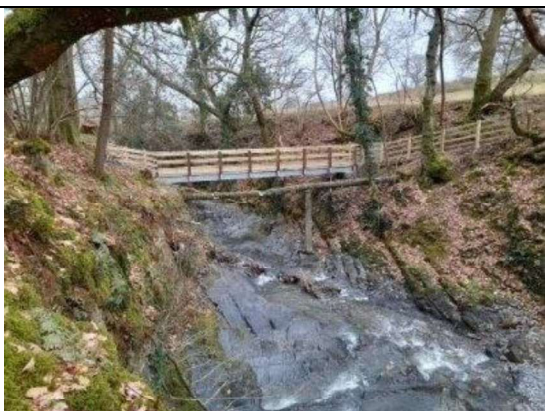

Access Improvement Grant – Reporting template

Please use a new sheet for each project / location.

Please copy and paste entire page for more templates.

Project title:	Location:
Cwm Biga Footbridge	Cwm Biga, Staylittle, Powys

Description of works completed:

- Installing a new footbridge in the area of Cwm Biga. The authority recently reopened a blocked footpath, and the route has become popular amongst locals. Concerns have been raised about a stream crossing that is difficult and dangerous.

Nov update:

- All of the surveying has been completed and routes identified for improvement.
- The Cwm Biga footbridge has been installed.
- Materials purchased and a contractor appointed to carry out the remaining improvement work, to install accessible path furniture. Completed.
- Improvements to drainage and surface of a byway – completed
- Activity completed early summer '23

March update:

- Additional culvert repair – provided materials for landowner installation.

Spend breakdown:

Total	Year 2		Notes
	Nov	March	
Budget	£2,000		
Activity 01/04/23 - 30/09/23	£1,354		
Activity 01/10/23 – March 2024		£723	
Staff 01/04/23 - March 2024		£0.00	
Total spend @ March 2024	£2,077		

Variance: +3.8%

Outputs:
(i.e. section 7 of the workplan.)

The project outputs will be:

- A new bridge at Cwm Biga and a further bridge downstream, where none have been in place before and which would facilitate access to the NRW forestry;
- Access improvements to the wider network of paths radiating out from Staylittle and connecting with Dylife and the Glyndwr's Way National Trail
- New signage.

This work is complete.

Photographic evidence – before / during:



Photographic evidence – after (not needed if an uncompleted multiyear project):



Some of the improvements:



