

Access Improvement Grant – Reporting template

Please use a new sheet for each project / location.

Please copy and paste entire page for more templates.

Project title: 1	Location:
Glyndwr's Way National Trail	Bwlch Y Sarnau

Description of works completed:
Replace rotting timber bridle boardwalk with stone sided culvert or metal beamed boardwalk. Long life replacement. December update - Works were carried out in August 2025 when the ground was sufficiently dry to allow access with heavy machinery. - The old timber bridleway boardwalk was removed and a large capacity culvert with stone sides installed. An aggregate surface was constructed on top of the culvert. - This structure will last for many years without the need for maintenance. - Project is completed and photos included - All payments completed. March update - No further action

Spend breakdown:			
Total	Year 1 / claims		Notes
	December '25	March '26	
Budget	£6,500		
Activity 01/04/25 -30/11/24	£5,701.00		
Activity 01/12/25 - March '26		£0.00	
Total claim (Dec/March)	£5,701.00	£0.00	
Total project spend	£5,701.00		
Variance: 0.87% of budget Explanation: Costs within budget by a value of £799.00			

Outputs:
<i>(What are the final outputs? Were the expected outputs from the work plan achieved / surpassed? If a multiyear project, highlight the outputs to date and advise if it is on track for project as a whole)</i>

Photographic evidence – before / during:



Photographic evidence – after (not needed if an uncompleted multiyear project):



Access Improvement Grant – Reporting template

Please use a new sheet for each project / location.

Please copy and paste entire page for more templates.

Project title: 2	Location:
Glyndwr's Way National Trail	Llangynllo and Llanwddyn

Description of works completed:
Replace old field gates on bridleway with high latch hunt gates to facilitate equestrian access. Replace stiles with gates (3 anticipated). December update Llangynllo. • Works were carried out in October to replace old field gates on a section of Glyndwr's Way with bridleway status. 7 high latch field gates were installed as part of a wider project in the area. This will provide easier access for equestrians and cyclists to the Beacon Hill area that the National Trail traverses. • Project is completed. • All payments completed. • Photos not currently available. Llanwyddan. • Works were carried out in November to replace three stiles with self-closing galvanised pedestrian gates on a section of Glyndwr's Way with footpath status. This will provide easier access for walkers in this popular area close to Lake Vyrnwy. • Project is completed. • Payments are not completed • Photos attached. March update Llangynllo • Photographs included Llanwyddan • Payments included below

Spend breakdown:			
Total	Year 1 / claims		Notes
	December '25	March '26	
Budget	£6,000		
Activity 01/04/25 -30/11/24	£4,739.00		
Activity 01/12/25 - March '26		£1,500.00	
Total claim (Dec/March)	£4,739.00	£1,500.00	
Total project spend (to date)	£6,239.00		

Variance: 104% of budget
Explanation: n/a

Outputs:

(What are the final outputs? Were the expected outputs from the work plan achieved / surpassed? If a multiyear project, highlight the outputs to date and advise if it is on track for project as a whole)

Photographic evidence – before / during:



Llanwyddan.

Photographic evidence – after (not needed if an uncompleted multiyear project):



Llanwyddan.



(above right and below) - 7 x hunt gates at Llangunllo



Access Improvement Grant – Reporting template

Please use a new sheet for each project / location.

Please copy and paste entire page for more templates.

Project title:3	Location:
Glyndwr's Way National Trail	Bryntail Bridge, Llanidloes Without

Description of works completed:
Phase 1 design (25/26) and Phase 2 construction (26/27). A mixed construction bridge, with metal main beams (do not need replacement) and a superstructure of oak. Work to include: Replace beam bolts. Replace all oak superstructure apart from deck (renewed in 2022). Full scaff. needed. (257/181(A)/1). Match funding with National Trail via NRW (£6,026), 2025/26 and intended match with NRW funding for construction phase (total project construction of £148,350k). December update • Building on some initial design work within this fin year, a further period of more focussed time will be allocated over December/January. • No external contractors/suppliers relating to the project have been raised by EDS to date. • Work is currently ongoing on the project programme, inspection report incl. recommendations for remedial works & remedial works cost estimates – this should hopefully be available for comment in mid-late January. March update: • Ongoing from above • No images applicable

Spend breakdown:			
Total	Year 1 / claims		Notes
	December '25	March '26	
Budget	£2,009.00		
Activity 01/04/25 -30/11/24	£0.00		
Activity 01/12/25 - March '26		£1,885.56	
Total claim (Dec/March)	£0.00	£1,885.56	
Total project spend (to date)	£1,885.56		

Variance: -6%

Explanation: n/a

Outputs:
<i>(What are the final outputs? Were the expected outputs from the work plan achieved / surpassed? If a multiyear project, highlight the outputs to date and advise if it is on track for project as a whole)</i>

--

Photographic evidence – before / during:
Photographic evidence – after (not needed if an uncompleted multiyear project):

Access Improvement Grant – Reporting template

Please use a new sheet for each project / location.
Please copy and paste entire page for more templates.

Project title:4	Location:
Dolfor Lock	Newtown

Description of works completed: Renovation of a canal bridge crossing the Montgomery Canal, which has heritage value and provides a key link within the community trails / public rights of way network on the outskirts of Newtown. Work will involve lime mortar repair and renovation which align with heritage work requirement, as noted in the options report. December update • Specification and tender process complete • Contractors appointed (Reynolds Construction) • Vegetation clearance around site undertaken ahead of practical work delivery (Oct) • On site work underway (Nov) • On site work completed (early Dec) • Invoice against works being reviewed by PCC Engineering Design Service, as part of standard procedure within contract management and for agreement of additional contract costs incurred as part of the specification – e.g additional 850 bricks needed to complete work. • Pre-Christmas completion of paperwork anticipated. March update: • EDS – repair works completed to satisfactory standard (26/02/26) • EDS approve invoice for contractor £31,540.27 • Hessian sheet protecting bridge repairs (lime mortar) from elements in place until spring • Engineer inspection needed on removal of hessian sheeting • Further inspection needed to ensure lime mortar has reached full strength • H&S file, maintenance manual and as-built drawing to follow from EDS. See comments below. I'll have to get some pictures from [REDACTED] I think we've already discussed but note that there will be EDS costs for the further inspections.
--

Spend breakdown:


Total	Year 1 / claims		Notes
	December '25	March '26	
Budget	£40,000.00		
Activity 01/04/25 -30/11/25	£8,365.83		
Activity 01/12/25 - March '26		£31,847.87	
Total claim (Dec/March)	£8,365.83	£31,847.87	
Total project spend (to date)	£40,213.70		

Variance: +0.5%

Explanation: n/a

Outputs:
<i>(What are the final outputs? Were the expected outputs from the work plan achieved / surpassed? If a multiyear project, highlight the outputs to date and advise if it is on track for project as a whole)</i>

Photographic evidence -- before / during:

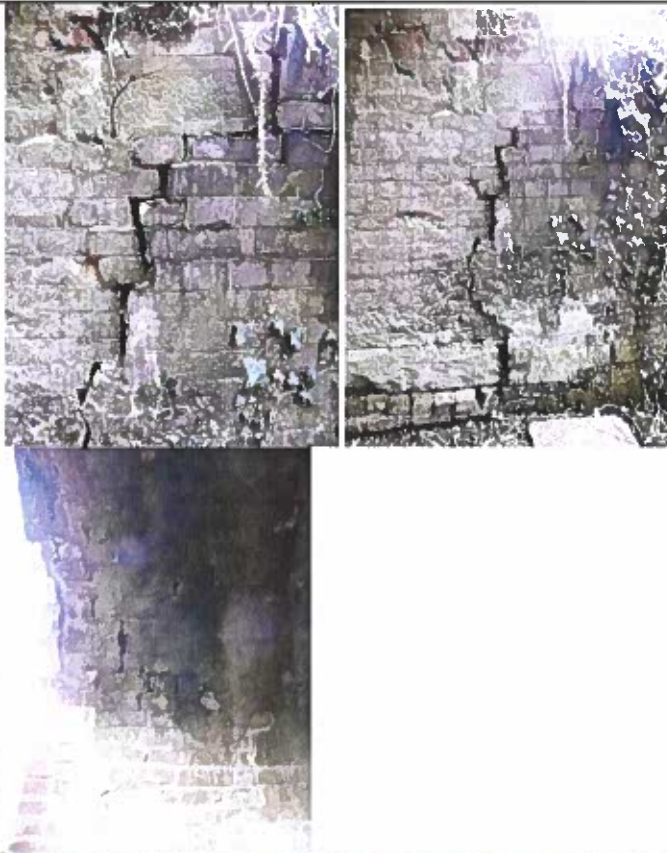

Photographic evidence – after (not needed if an uncompleted multiyear project):





Access Improvement Grant – Reporting template

Please use a new sheet for each project / location.

Please copy and paste entire page for more templates.

Project title: 5	Location:
Marteg Bridge	St Harmon

Description of works completed:
Phase 1 design (25/26) and Phase 2 implementation (26/27). Wye Valley Walk bridge with metal beams and handrails along with a timber deck. Handrails damaged and patch repaired to date. Consideration need to be given to the large drop to water (River Wye) (Path 144/245/1)
December update
- Phase 1 design work underway, via PCC Engineering Design Service (EDS) - Internal billing not yet actioned for time to date
March update
- A specification has been devised for the work needed to the bridge and has been signed off by the Council's Engineering Design team. This will be used to procure the work in 2026-27. - No images applicable

Spend breakdown:			
Total	Year 1 / claims		Notes
	December '25	March '26	
Budget	£3,090.63		
Activity 01/04/25 -30/11/25	£0.00		
Activity 01/12/25 - March '26		£1,758.15	

Total claim (Dec/March)	£0.00	£1,758.15	
Total project spend	£1,758.15		
Variance: -43%			
Explanation: as above			

Outputs:
<i>(What are the final outputs? Were the expected outputs from the work plan achieved / surpassed? If a multiyear project, highlight the outputs to date and advise if it is on track for project as a whole)</i>

Photographic evidence – before / during:
Photographic evidence – after (not needed if an uncompleted multiyear project):

Access Improvement Grant – Reporting template

Please use a new sheet for each project / location.

Please copy and paste entire page for more templates.

Project title: 6	Location:
Tyn Ddol Bridge,	Llanbadarn Fawr

Description of works completed:
Phase 1 design (25/26) and Phase 2 construction (26/27). 27m Suspension bridge, eastern tower concrete starting to be undercut/river scour and rot in base of towers. (Path 127/106/)
December update - Phase 1 design work underway, via PCC Engineering Design Service (EDS) - Internal billing not yet actioned for time to date
March update - No costs have been included as other bridges have taken priority and there is a general need to review the options in terms of what we do i.e. it is not guaranteed that the bridge will be replaced. - No images applicable

Spend breakdown:

Total	Year 1 / claims		Notes
	December '25	March '26	
Budget	£5,563.13		
Activity 01/04/25 -30/11/25	£0.00		
Activity 01/12/25 - March '26		£0.00	
Total claim (Dec/March)	£0.00	£0.00	
Total project spend	£0.00		

Variance: -100%

Explanation: as noted above

Outputs:

(What are the final outputs? Were the expected outputs from the work plan achieved / surpassed? If a multiyear project, highlight the outputs to date and advise if it is on track for project as a whole)

Photographic evidence – before / during:

Photographic evidence – after (not needed if an uncompleted multiyear project):

Access Improvement Grant – Reporting template

Please use a new sheet for each project / location.

Please copy and paste entire page for more templates.

Project title: 7	Location:
Severn Arms bridge	Penybont

Description of works completed:

An important and popular community/ amenity asset (25m bridge), linking to the football pitch & trotting race grounds. Work includes replacement of timber deck, handrail repair, (2 metal beams ok). New long life deck capable of spanning between 2 beams. Main river lthon. River approx 20m wide and 5m from deck to water. Consideration needed around weight of deck on beams.

December update

- Phase 1 design work underway, via PCC Engineering Design Service (EDS)
- Internal billing not yet actioned for time to date

March update

- The Council's Engineering Design team have reviewed the options for materials to re-deck the bridge. These are based on modern materials with lower weights than timber

and long lifespans, as it receives high usage for concentrated periods when there are community events and sports fixtures on the greenspace to which it gives access.

- Costings have been devised and the environmental and flood risk consents are being progressed, with a view to carrying out the work in summer 2026
- No images applicable

Spend breakdown:

Total	Year 1 / claims		Notes
	December '25	March '26	
Budget	£6,181.25		
Activity 01/04/25 -30/11/25	£0.00		
Activity 01/12/25 - March '26		£3,806.11	
Total claim (Dec/March)	£0.00	£3,806.11	
Total project spend	£3,806.11		

Variance: -38%

Explanation: as noted above

Outputs:

(What are the final outputs? Were the expected outputs from the work plan achieved / surpassed? If a multiyear project, highlight the outputs to date and advise if it is on track for project as a whole)

Photographic evidence – before / during:

Photographic evidence – after (not needed if an uncompleted multiyear project):

Access Improvement Grant – Reporting template

Please use a new sheet for each project / location.

Please copy and paste entire page for more templates.

Project title: 8	Location:
A selection of small bridges	Llanidloes cluster

Description of works completed:

A selection of four small bridges (5-10m) that will open up a number of well used community trails and linkage to a the greater path network. Many of the bridges can be installed with the support of our active Countryside Volunteer programme and thus provide value for money across the installations

Locations to include: Dolgwyddel, Staylittle; Draenen Ddu, Trefeglwys; Tan Hinion near Old Hall; Summerfield Park, Llanidloes

December update

- Materials identified and orders placed.
- Contractor quotes sought, with accompanying site visits completed
- Installation in new year, weather and contractor dependant

March update

- Material ordered and contractors appointed for installations, when weather permits in the spring/summer
- An additional bridge has been added to the cluster – an unexpected closure of an 18m bridge for health and safety purposes (Glyn bridge). As a significant link in the surrounding path network and on a very popular route for the community and visitors staying at nearby holiday accommodation, the provision of a new bridge is considered a priority.

Spend breakdown:

Total	Year 1 / claims		Notes
	December '25	March '26	
Budget	£26,885.00		
Activity 01/04/25 -30/11/25	£0.00		
Activity 01/12/25 - March '26		£42,819.59	
Total claim (Dec/March)	£0.00	£42,819.59	
Total project spend (to date)	£42,819.59		

Variance: +59%

Explanation: as noted above

Outputs:

(What are the final outputs? Were the expected outputs from the work plan achieved / surpassed? If a multiyear project, highlight the outputs to date and advise if it is on track for project as a whole)

Photographic evidence – before / during:

--

Photographic evidence – after (not needed if an uncompleted multiyear project):

--

Access Improvement Grant – Reporting template

Please use a new sheet for each project / location.

Please copy and paste entire page for more templates.

Project title: 9	Location:
A selection of small bridges	Cemmaes cluster

Description of works completed:
A selection of three small bridges (5-10m) that will open up a number of well used community trails and linkage to a the greater path network. Many of the bridges can be installed with the support of our active Countryside Volunteer programme and thus provide value for money across the installations Locations to include: Commins metal bridge, Cemmaes timber bridge (including associated path work); Cemmaes concrete bridge. December update • Materials identified and orders placed. • Contractor quotes sought, with accompanying site visits completed • Installation in new year, weather and contractor dependant. March update: • Materials ordered • Contractor appointed • Installations to be completed when weather improves and river levels permit, giving consideration for landowner access and ground conditions.

Spend breakdown:			
Total	Year 1 / claims		Notes
	December '25	March '26	
Budget	£30,000.00		
Activity 01/04/25 -30/11/25	£0.00		
Activity 01/12/25 - March '26		£29,025.05	
Total claim (Dec/March)	£0.00	£29,025.05	
Total project spend	£29,025.05		

Variance: -3%

Explanation: n/a

Outputs:
<i>(What are the final outputs? Were the expected outputs from the work plan achieved / surpassed? If a multiyear project, highlight the outputs to date and advise if it is on track for project as a whole)</i>

Photographic evidence – before / during:
Photographic evidence – after (not needed if an uncompleted multiyear project):

Access Improvement Grant – Reporting template

Please use a new sheet for each project / location.

Please copy and paste entire page for more templates.

Project title: 10	Location:
A selection of bridges	Gregynog / Llanfair Caereinion cluster

Description of works completed: A selection of four bridges (10-16m) that will open up a number of well used community trails and linkage to the greater path network. Installed with the support of our active Countryside Volunteer programme, where appropriate to provide value for money across the installations Locations to include: Gregynog Estate bridge (design 26/27) Tan House Farm footbridge (design 26/27) (Llanfair Caereinion) Gregynog Estate East River bridge - just needs re-decking Gregynog Estate mill race - ordered Gregynog Estate west bridge - ordered December update - Materials identified and orders placed. - Installation will take place with the Countryside Volunteers March update - Gregynog Estate mill race - ordered and will be installed by volunteers during 2026 - Gregynog Estate west bridge - ordered and will be installed by volunteers during 2026
--

Spend breakdown:			
Total	Year 1 / claims		Notes
	December '25	March '26	
Budget	£7,000.00		
Activity 01/04/25 -30/11/25	£0.00		
Activity 01/12/25 - March '26		£5,859.00	
Total claim (Dec/March)	£0.00	£5,859.00	
Total project spend	£5,859.00		

Variance: -16%

Explanation: n/a

Outputs: <i>(What are the final outputs? Were the expected outputs from the work plan achieved / surpassed? If a multiyear project, highlight the outputs to date and advise if it is on track for project as a whole)</i>
--

Photographic evidence – before / during:

Photographic evidence – after (not needed if an uncompleted multiyear project):

Access Improvement Grant – Reporting template

Please use a new sheet for each project / location.
Please copy and paste entire page for more templates.

Project title: 11	Location:
Wye Valley Walk bridge -	Newbridge to Builth Section

Description of works completed: Construction of two new bridges - 1x 9m bridge (040/3/1) and 1x 10m bridge (040/4/1) December update - Materials identified and orders placed. - Contractor quotes sought, with accompanying site visits completed March update WWW steel/recycled plastic 8m bridge at NGR 300307:255458. - Steel and plastic ordered and awaiting delivery - Contractor (Mike Hulin) PO for works issued ready to start as weather allows. - Landowner consultation access agreed. WWW steel/recycled plastic 8m bridge at NGR 300074:254471 - Steel and plastic ordered and awaiting delivery - Contractor (Mike Hulin) PO for works issued ready to start as weather allows. - Landowner consultation difficult. may need upfront financial agreement and/or use of Statutory powers for vehicular access.
--

Spend breakdown:			
Total	Year 1 / claims		Notes
	December '25	March '26	
Budget	£20,000.00		
Activity 01/04/25 -30/11/25	£0.00		
Activity 01/12/25 - March '26		£19,762.68	
Total claim (Dec/March)	£0.00	£19,762.68	
Total project spend	£19,762.68		
Variance: -1%			
Explanation: n/a			

Outputs:

(What are the final outputs? Were the expected outputs from the work plan achieved / surpassed? If a multiyear project, highlight the outputs to date and advise if it is on track for project as a whole)

Photographic evidence – before / during:

Photographic evidence – after (not needed if an uncompleted multiyear project):

Access Improvement Grant – Reporting template

Please use a new sheet for each project / location.

Please copy and paste entire page for more templates.

Project title: 12	Location:
The Nea, Offa's Dyke Path	

Description of works completed:

Design and capital work to Offa's Dyke Path at the Nea. A section of the National Trails which is severely damaged by badger setts. Activity to be match funded by CADW and other sources.

December update

- Ecologist appointed to undertake an onsite survey and report
- A technical report will then be compiled (following site surveys), to determine next steps.
- An appropriate work to be scheduled following receipt of the reports
- This is a partnership project with CADW, ODP Conservation Project in the first instance and scale of further, future intervention will be determined by available funds, (from a wider source)

March update

- Ecology report received 08.01.26
- Site meeting held 13.01.26 – attendees: NTO, ODCP Project Officer, CADW rep, groundworks, and ecology contractors
- Estimate of groundworks costs and technical report quote received 27.01.26
- Technical report / ground works method statement for works received 22.02.26
- POs – Morph Ecological £1867.80 P197837, Dean Martin Contractors Ltd £680.00 P204526
- Next steps – draw up specification and invite quotes for work. Awaiting indicative costs for ecology consultant during works and for licence application process.
- Investigate sources of funding – CADW have indicated agreed contribution.
- The underspend of practical works has enabled the appointment of a contractor for eroding river bank works and the installation of a bridge at Stonehouse farm.

Spend breakdown:

Total	Year 1 / claims		Notes
	December '25	March '26	
Budget	£10,000.00		
Activity 01/04/25 -30/11/25	£0.00		
Activity 01/12/25 - March '26		£6,926.80	
Total claim (Dec/March)	£0.00	£6,926.80	
Total project spend	£6,926.80		

Variance: -30%

Explanation: as noted above

Outputs:

(What are the final outputs? Were the expected outputs from the work plan achieved / surpassed? If a multiyear project, highlight the outputs to date and advise if it is on track for project as a whole)

Photographic evidence – before / during:



Photographic evidence – after (not needed if an uncompleted multiyear project):

Access Improvement Grant – Reporting template

Please use a new sheet for each project / location.

Please copy and paste entire page for more templates.

Project title: 13	Location:
Llandrindod Wells Green Space	Llandrindod Wells

Description of works completed: Llandrindod town centre PROW and future wildlife site (PCC Education). To improve access in a popular town greenspace by addressing the poor condition of the access paths, in an area where biodiversity enhancements will be delivered via phased investment (non AIG). This will involve resurfacing the paths and installation of drainage where required (section 1) Scrape off 150m of existing pathway. Lay new pipe to 2 ditch crossings. Build 4 headwalls & path edgings with conservation sacks. Stone pathway 1.5m with stone, average depth 75mm. (Section 2): Scrape off 110m of pathway. Remove timber. Lay stone 1.5m wide 75mm depth. December update - Appointed contractor, Gary Bevan Groundworks, will be starting week beginning 5th January 2026. - Work will also address the following - a resident whose garden keep flooding and a dangerous tree that is overhanging their garden. This will include ditch clearing more stone and drainage pipe and the felling of the tree. March update - Path improvements completed (early Feb) - Images to follow

Spend breakdown:			
Total	Year 1 / claims		Notes
	December '25	March '26	
Budget	£12,000.00		
Activity 01/04/25 -30/11/25	£0.00		
Activity 01/12/25 - March '26		£12,000.00	
Total claim (Dec/March)	£0.00	£12,000.00	
Total project spend	£12,000.00		
Variance: 0%			
Explanation: n/a			

Outputs: <i>(What are the final outputs? Were the expected outputs from the work plan achieved / surpassed? If a multiyear project, highlight the outputs to date and advise if it is on track for project as a whole)</i>

Photographic evidence – before / during:

Photographic evidence – after (not needed if an uncompleted multiyear project):

Access Improvement Grant – Reporting template

Please use a new sheet for each project / location.
Please copy and paste entire page for more templates.

Project title:14	Location:
Llansilin community trails	

Description of works completed: Brilliant Basics match funding - community trails project in Llansilin community. Work to include the development of a series of promoted community trails from the settlement hub. December update - All paths within the community have been surveyed, with detail being added to the CAMS database. - Selected trails have been shortlisted. - Landowner negotiations, agreed on the majority of routes - Installations with volunteers to take place throughout 2026 (as part of the wider project) March update - Materials ordered, ahead of volunteer installation work days

Spend breakdown:			
Total	Year 1 / claims		Notes
	December '25	March '26	
Budget	£2,000.00		
Activity 01/04/25 -30/11/25	£0.00		
Activity 01/12/25 - March '26		£2,000.00	
Total claim (Dec/March)	£0.00	£2,000.00	
Total project spend	£2,000.00		
Variance: 0%			
Explanation: n/a			

Outputs: <i>(What are the final outputs? Were the expected outputs from the work plan achieved / surpassed? If a multiyear project, highlight the outputs to date and advise if it is on track for project as a whole)</i>
--

Photographic evidence – before / during:
--

Access Improvement Grant – Reporting template

Please use a new sheet for each project / location.

Please copy and paste entire page for more templates.

Project title:15	Location:
Llanwrtyd Wells community trails	

Description of works completed:
Brilliant Basics match funding - community trails project in Llanwrtyd community. Work to include the development of a series of promoted community trails from the settlement hub.
December update - The majority of identified paths within the community have been surveyed, with detail being added to the CAMS database. - Selected trails are being shortlisted - Landowner negotiations underway - Installations with volunteers to take place throughout 2026 (as part of the wider project) March update - Materials ordered, ahead of volunteer installation work days

Spend breakdown:			
Total	Year 1 / claims		Notes
	December '25	March '26	
Budget	£2,000.00		
Activity 01/04/25 -30/11/25	£0.00		
Activity 01/12/25 - March '26		£2,000.00	
Total claim (Dec/March)	£0.00	£2,000.00	
Total project spend	£2000.00		

Variance: 0%

Explanation: n/a

Outputs:
<i>(What are the final outputs? Were the expected outputs from the work plan achieved / surpassed? If a multiyear project, highlight the outputs to date and advise if it is on track for project as a whole)</i>

Photographic evidence – before / during:
Photographic evidence – after (not needed if an uncompleted multiyear project):

Access Improvement Grant – Reporting template

Please use a new sheet for each project / location.

Please copy and paste entire page for more templates.

Project title: 16	Location:
Carreghofa community trails	

Description of works completed:
Brilliant Basics match funding - community trails project in Carreghofa community. Work to include the development of a series of promoted community trails from the settlement hub.
December update - All paths within the community have been surveyed, with detail being added to the CAMS database. - Selected trails are being shortlisted with the Town Council - Landowner negotiations and purchase of materials will follow in early 2026 - Installations with volunteers to take place throughout 2026 (as part of the wider project) March update - Materials ordered, ahead of volunteer installation work days

Spend breakdown:			
Total	Year 1 / claims		Notes
	December '25	March '26	
Budget	£2,000.00		
Activity 01/04/25 -30/11/25	£0.00		
Activity 01/12/25 - March '26		£2,000.00	
Total claim (Dec/March)	£0.00	£2000.00	
Total project spend	£2000.00		

Variance: 0%

Explanation: n/a

Outputs:
<i>(What are the final outputs? Were the expected outputs from the work plan achieved / surpassed? If a multiyear project, highlight the outputs to date and advise if it is on track for project as a whole)</i>

Photographic evidence – before / during:
Photographic evidence – after (not needed if an uncompleted multiyear project):

Access Improvement Grant – Reporting template

Please use a new sheet for each project / location.

Please copy and paste entire page for more templates.

Project title: 17	Location:
Ann Griffiths Walk - linking trails	

Description of works completed:
The creation of community trails that link to/around the Ann Griffiths Walk and improvement to this well used cultural recreational trail, through improved signage etc.
December update - Materials identified and orders placed for two bridges that support the path network. - Contractor quotes sought, with accompanying site visits completed - Installation of bridges to take place in 2026. March update - Materials ordered - Contractor appointed - Installations to be completed when weather improves and river levels permit, giving consideration for landowner access and ground conditions.

Spend breakdown:			
Total	Year 1 / claims		Notes
	December '25	March '26	
Budget	£2,000		
Activity 01/04/25 -30/11/25	£0.00		
Activity 01/12/25 - March '26		£5,403.74	
Total claim (Dec/March)	£0.00	£5,403.74	
Total project spend	£5,403.74		

Variance: +170%

Explanation: as noted above

Outputs:
<i>(What are the final outputs? Were the expected outputs from the work plan achieved / surpassed? If a multiyear project, highlight the outputs to date and advise if it is on track for project as a whole)</i>

Photographic evidence – before / during:
Photographic evidence – after (not needed if an uncompleted multiyear project):

Access Improvement Grant – Reporting template

Please use a new sheet for each project / location.

Please copy and paste entire page for more templates.

Project title: 18	Location:
Small bridges/boardwalks	Various locations

Description of works completed:
Enabling enhanced involvement of individuals within the revised Countryside Volunteer programme, linking with a reactive programme of small bridge/boardwalk replacement or creation (1-5m), supported by officer works days. This will build on previous development of the volunteer handbook. December update Ystradgynlais bridge • Bridge installation contractor appointed, Matthew Thomas. • Landowner negotiation currently underway around footbridge, regarding future use /access. • Additional kissing gate and fencing required at one end of the bridge. March update FP 090/3/1 Ystradgynlais. • Replace dilapidated stile with KG and re fence as required. Replace/improve sleeper bridge at NGR 278634:210909 • Contract and works schedule issued • Kissing gate and fencing completed. • Landowner required replacement bridge to be up to agricultural vehicular standard which was beyond scope of the project budget. Sleepers have been overlaid with recycled plastic decking fit for pedestrian use only at this time. This links in with the Brynygroes development diversion package.

Spend breakdown:

Total	Year 1 / claims		Notes
	December '25	March '26	
Budget	£7,120.99		
Activity 01/04/25 -30/11/25	£0.00		
Activity 01/12/25 - March '26		£4,000.00	
Total claim (Dec/March)	£0.00	£4,000.00	
Total project spend	£4000.00		

Variance: -44%

Explanation: volunteer programme has focussed more on bridge re-decking, than small bridge replacement,

Outputs:

(What are the final outputs? Were the expected outputs from the work plan achieved / surpassed? If a multiyear project, highlight the outputs to date and advise if it is on track for project as a whole)

Photographic evidence – before / during:

Photographic evidence – after (not needed if an uncompleted multiyear project):

Access Improvement Grant – Reporting template

Please use a new sheet for each project / location.

Please copy and paste entire page for more templates.

Project title: 19	Location:
Project Management - bridges	

Description of works completed:
Project Management @ 15% flat rate
December update - Staff time for oversight of the bridge programme, particularly in relation to the AIG award - Remaining costs to be claimed within the final claim March update - As above, balance claimed at year end

Spend breakdown:			
Total	Year 1 / claims		Notes
	December '25	March '26	
Budget	£34,650.00		
Activity 01/04/25 -30/11/25	£17,779.96		
Activity 01/12/25 - March '26		£16,870.04	
Total claim (Dec/March)	£17,779.96	£16,870.04	
Total project spend (to date)	£34,650.00		

Variance: 0%

Explanation: n/a

Outputs:
<i>(What are the final outputs? Were the expected outputs from the work plan achieved / surpassed? If a multiyear project, highlight the outputs to date and advise if it is on track for project as a whole)</i>

Photographic evidence – before / during:
n/a
Photographic evidence – after (not needed if an uncompleted multiyear project):
n/a

Access Improvement Grant – Reporting template

Please use a new sheet for each project / location.

Please copy and paste entire page for more templates.

Project title: 20	Location:
Bridge programme resources	

Description of works completed:
The development of bridge programme assets (documentation) to support future management of the PROW network, including: working with PCC Engineering Design Service to create designs for standard bridges (to support procurement) - and the development of an inspection regime.
December update - Design specifications complete, small footbridges - Development for an inspection framework underway, with PCC Engineering Design Service. - Internal billing to be actioned March update - Development for an inspection framework, to support the frequency of bridge surveying by volunteers, staff and others, as required (framework delivered by PCC Engineering Design Service).

Spend breakdown:

Total	Year 1 / claims		Notes
	December '25	March '26	
Budget	£6,000.00		
Activity 01/04/25 -30/11/25	£0.00		
Activity 01/12/25 - March '26		£2,648.34	
Total claim (Dec/March)	£0.00	£2,648.34	
Total project spend	£2,648.34		

Variance: -56%

Explanation: Reduction in time allocated due to limited capacity of PCC Engineering Design Service

Outputs:
<i>(What are the final outputs? Were the expected outputs from the work plan achieved / surpassed? If a multiyear project, highlight the outputs to date and advise if it is on track for project as a whole)</i>

Photographic evidence – before / during:

Photographic evidence – after (not needed if an uncompleted multiyear project):

Access Improvement Grant – Reporting template

Please use a new sheet for each project / location.

Please copy and paste entire page for more templates.

Project title: 21	Location:
*Additional - Llangynog bridges	

Description of works completed:
Replacement of two bridges – Nant and Glan Yr Afon
December update - Materials identified and orders placed for two bridges that support the path network. - Contractor quotes sought, with accompanying site visits completed - Installation of bridges to take place in 2026. March update - Materials ordered - Contractor appointed - Installations to be completed when weather improves and river levels permit, giving consideration for landowner access and ground conditions.

Spend breakdown:			
Total	Year 1 / claims		Notes
	December '25	March '26	
Budget	£15,000.00		
Activity 01/04/25 -30/11/25	£0.00		
Activity 01/12/25 - March '26		£17,301.28	
Total claim (Dec/March)	£0.00	£17,301.28	
Total project spend	£17,301.28		
Variance: +15%			
Explanation: n/a			

Outputs:
<i>(What are the final outputs? Were the expected outputs from the work plan achieved / surpassed? If a multiyear project, highlight the outputs to date and advise if it is on track for project as a whole)</i>
